


VILLAGE OF BUTLER 2016 PAVING PROGRAM

ACCESS TO BUSINESSES DURING CONSTRUCTION

SEQUENCE OF CONSTRUCTION

*THE FOLLOWING SCHEDULE IS PRELIMINARY AND IS SUBJECT TO CHANGE. THIS SCHEDULE ASSUMES THAT CURB & GUTTER WORK, CURB RAMP WORK, UTILITY RELATED WORK, & DETOUR SIGN INSTALLATION ARE COMPLETED PRIOR TO THE BEGINNING OF MAINLINE PAVING OPERATIONS.

- PHASE 1 (6 Days)
 - +2 Days - Excavation (Limited Access to Driveways)
 - +1 Day - Paving (No Access to Driveways)
 - +3 Days - Pavement Curing Time (No Access to Driveways)
- PHASE 2 (6 Days)
 - +2 Days - Excavation (Limited Access to Driveways)
 - +1 Day - Paving (No Access to Driveways)
 - +3 Days - Pavement Curing Time (No Access to Driveways)
- PHASE 2A (6 Days)
 - +2 Days - Excavation (Limited Access to Driveways)
 - +1 Day - Paving (No Access to Driveways)
 - +3 Days - Pavement Curing Time (No Access to Driveways)
- PHASE 2B (6 Days)
 - +2 Days - Excavation (Limited Access to Driveways)
 - +1 Day - Paving (No Access to Driveways)
 - +3 Days - Pavement Curing Time (No Access to Driveways)
- PHASE 2C (6 Days)
 - +2 Days - Excavation (Limited Access to Driveways)
 - +1 Day - Paving (No Access to Driveways)
 - +3 Days - Pavement Curing Time (No Access to Driveways)
- PHASE 2D (6 Days)
 - +2 Days - Excavation (Limited Access to Driveways)
 - +1 Day - Paving (No Access to Driveways)
 - +3 Days - Pavement Curing Time (No Access to Driveways)
- PHASE 2E (4 Days)
 - +2 Days - Excavation (Limited Access to Driveways)
 - +1 Day - Binder Paving (Limited Access to Driveways)
 - +1 Day - Surface Paving (Limited Access to Driveways)

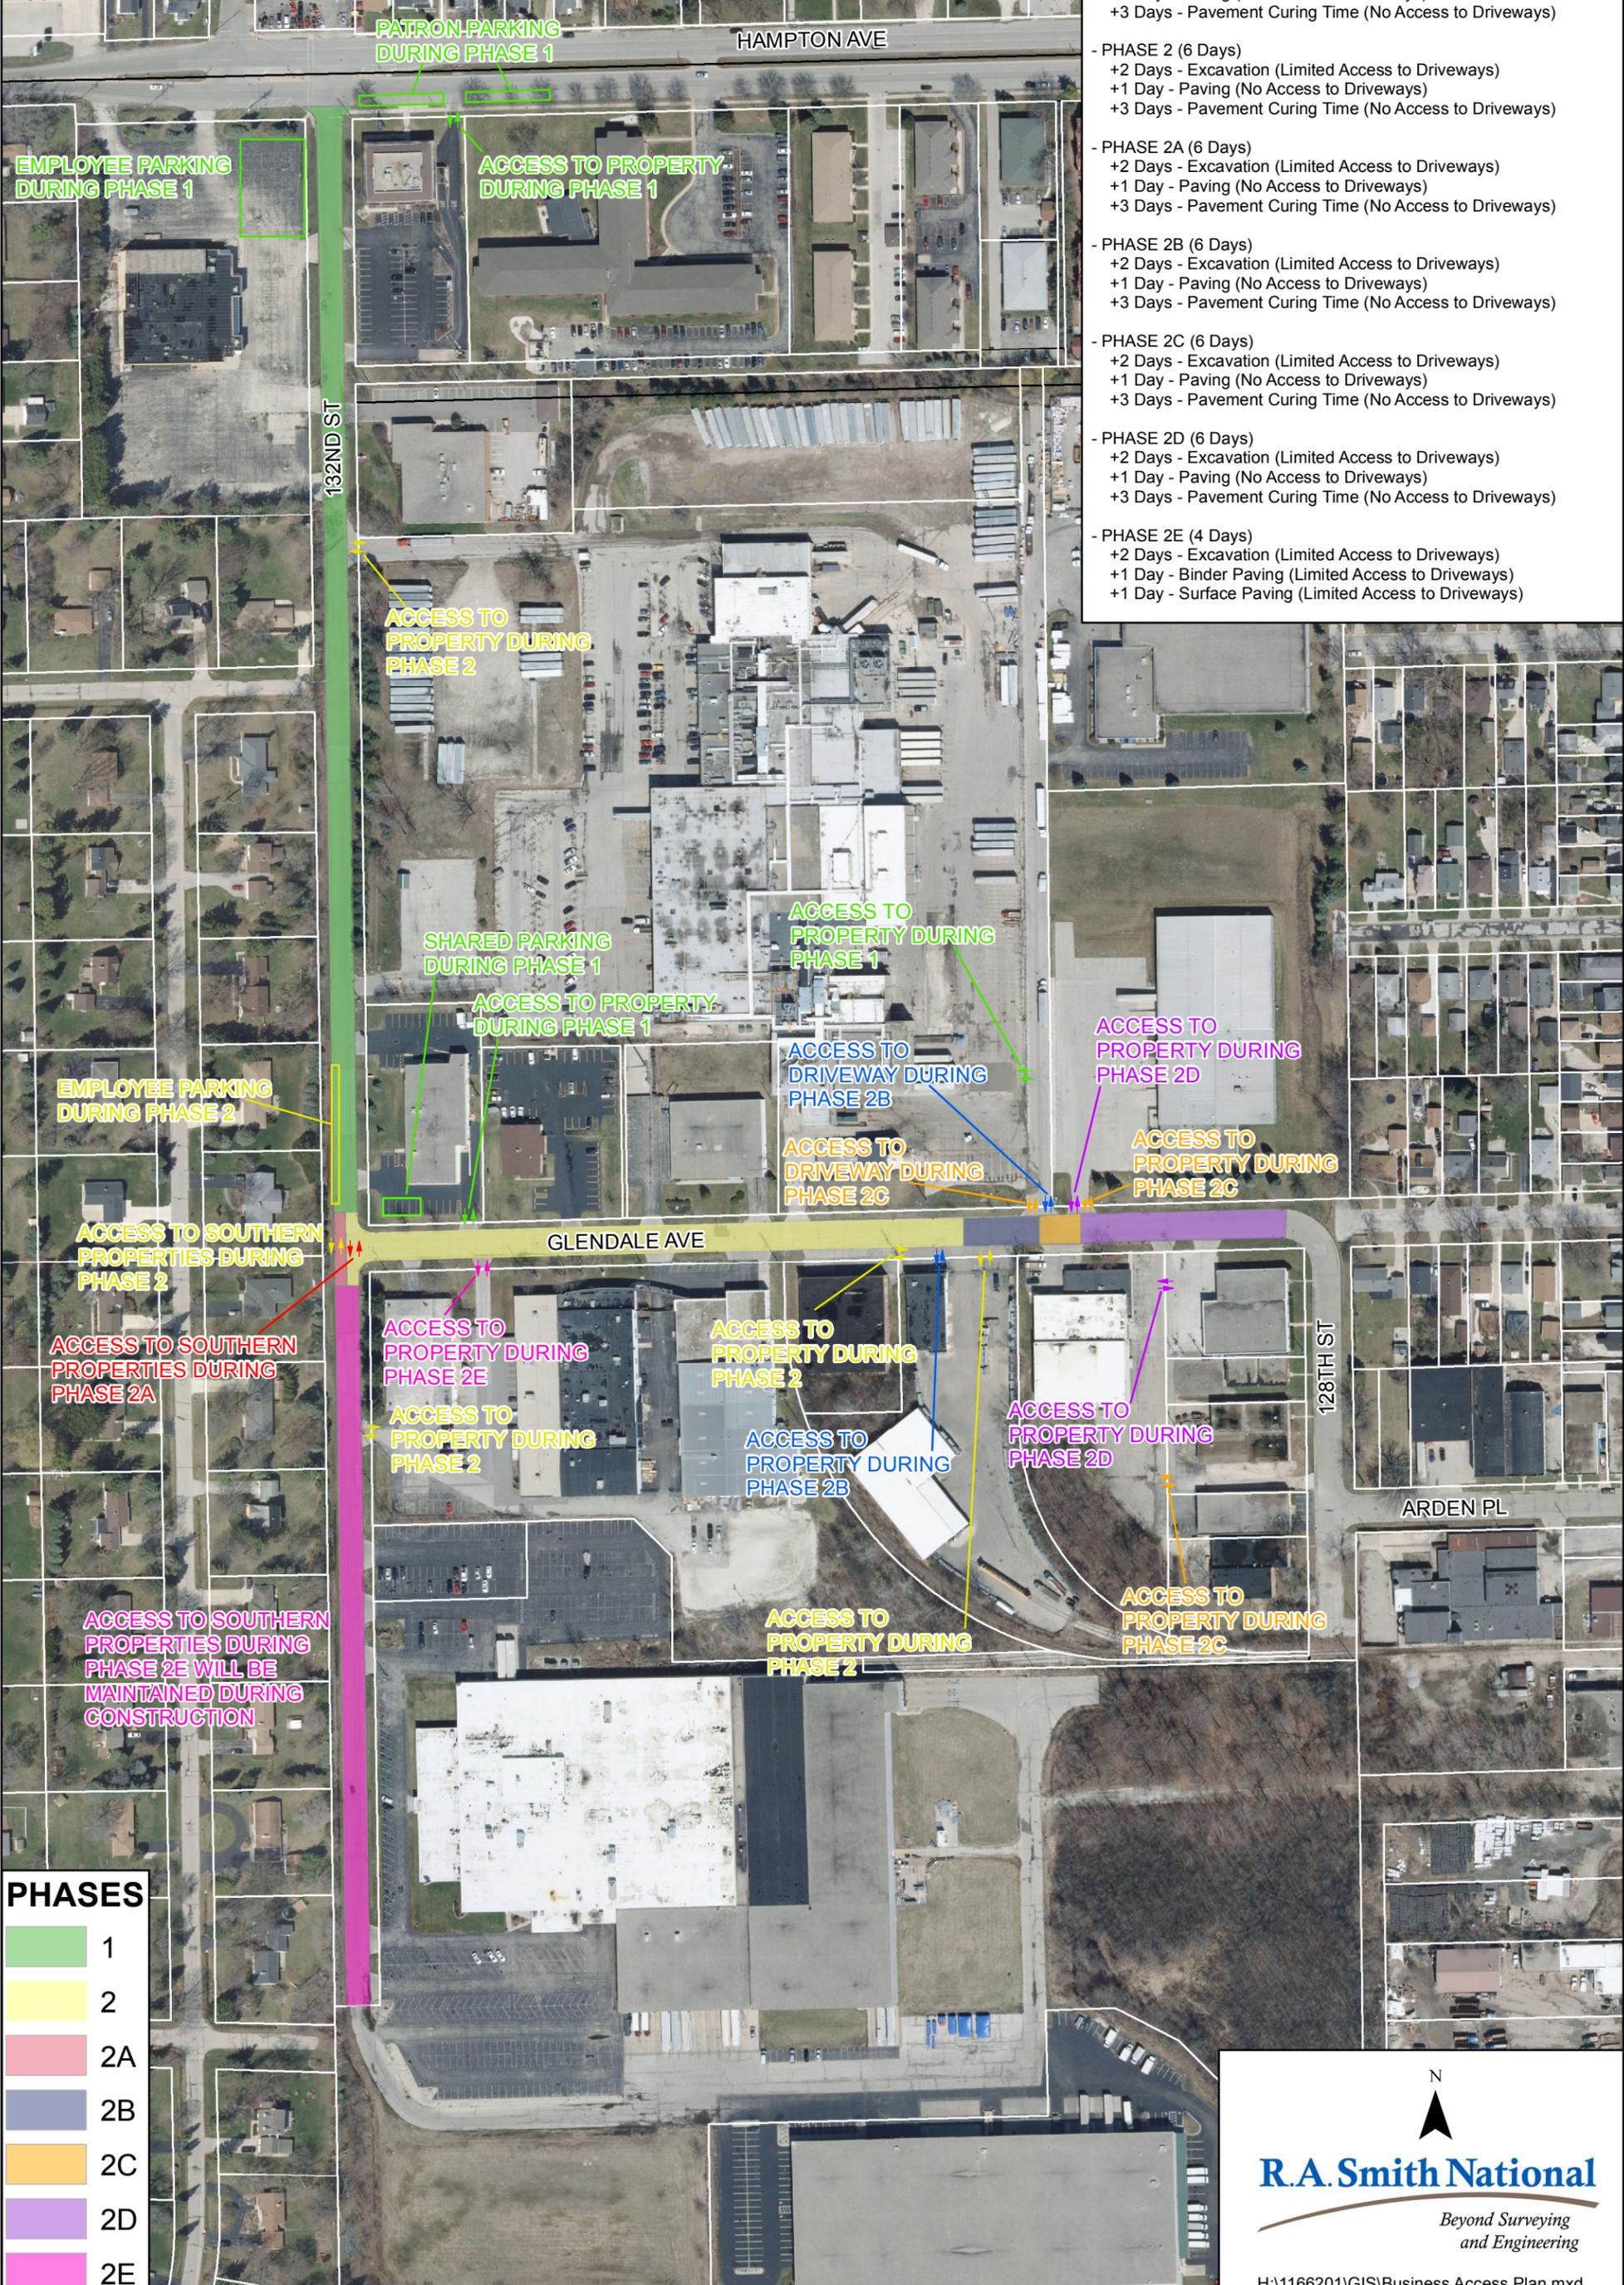

PHASES	
	1
	2
	2A
	2B
	2C
	2D
	2E

N

R.A. Smith National
*Beyond Surveying
and Engineering*

H:\1166201\GIS\Business Access Plan.mxd
